



Modern Food Storage Facilities Project  
Directorate General of Food

Annual Procurement Plan for 2022-2023  
Version: 1

July 2022

  
29/07/22  
(মোঃ রেজাউল করিম সৈখ)  
সকল পরিচালক (জি-সিডি)  
আর্থিক খাদ্য সরবরাহের নির্দেশ দপ্তর  
খাদ্য অধিদপ্তর, ঢাকা

  
29/07/22  
মোঃ শাখাওয়াত হোসেন  
মহাপরিচালক  
খাদ্য অধিদপ্তর, ঢাকা

৩৮/৪

# Annual Procurement Plan

Year: 2022-2023

Budget: Development Goods

Ministry/Division  
Agency  
Procuring Entity Name & Code  
Project/Programme Name & Code

Ministry of Food  
Directorate General of Food  
Project Director  
Modern Food Storage Facilities Project

5015

Package No.	Description of Procurement Packages Goods	Unit	Qty	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estd. Cost in Lac Tk	Time Code for Process	Not Used in Goods	Tender Notice	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18		
GD-04	Purchase of office and ICT equipment for PMU and 8 Site offices	LS	LS	NCB/eGP	PD	IDA Credit	42.50	Planned dates Planned days		2-Nov-22 0	30-Nov-22 28	9-Jan-23 40	16-Jan-23 7	23-Jan-23 7	20-Feb-23 28	110	19-Aug-23 180		
GD-07	Laptop, Computer, Printer, Photocopier etc.	LS	LS	NCB/eGP	PD	IDA Credit	20.00	Planned dates Planned days Actual Dates		10-Oct-22 0	7-Nov-22 28	17-Dec-22 40	24-Dec-22 7	31-Dec-22 7	28-Jan-23 28	110	27-Jul-23 180		
GD-09	Procurement of Furniture for PMU and Silo offices	LS	LS	NCB/eGP	PD	IDA Credit	17.00	Planned dates Planned days Actual Dates		10-Oct-22 0	7-Nov-22 28	7-Dec-22 30	12-Dec-22 5	16-Dec-22 4	13-Jan-23 28	95	12-Jul-23 180		
GD-22	Supply of food testing laboratory apparatus and related equipment	LS	LS	ICB/eGP	PD	GOB	1,000.00	Planned dates Planned days Actual Dates		1-Jan-23 0	14-Feb-23 44	16-Mar-23 30	21-Mar-23 5	25-Mar-23 4	22-Apr-23 28	111	19-Oct-23 180		
Total							1,079.50												

Total 1,079.50

For GD-04,07,09: 50% of the DPP provisions are planned for this year.

No of Package  
Lac. BDT  
Total Goods 3 1,079.50  
Total Works 1 32,660.40  
Total Services 5 440.00  
Total for year 2022-2023 34,179.90

Engr. Syed Rafiqul Alam  
Senior Procurement Specialist  
Modern Food Storage Facilities Project  
Directorate General of Food

*Rafiq*  
27/7/2022

(Muhammed Adnan Rahman)  
Deputy Project Director  
Modern Food Storage Facilities Project  
Directorate General of Food, Dhaka

*a.d*  
27/7/22

(মোঃ মোজাউল হকিয়া বেগম)  
প্রকল্প পরিচালক (উপ-সচিব)  
প্রকল্প বাস্তবায়নের নিয়ন্ত্রণ প্রকল্প  
আঞ্চলিক বাস্তু সঞ্চালকালয়  
আবাস অধিদপ্তর, ঢাকা।

*Mojib*  
29/9/22

মোঃ শাখাওয়াত হোসেন  
সহপরিচালক  
আবাস অধিদপ্তর, ঢাকা

*Shakawat*  
29/9/22

*10/10*

## Annual Procurement Plan

Ministry/Division

: Ministry of Food

Year: 2022-23

Agency

: Directorate General of Food

Project/Programme Name & Code

: Project Director

Project/Programme Name & Code : Modern Food Storage Facilities Project 5015

Budget: Development Works

Package No.	Description of Procurement Packages Works	Unit	Qty	Procurement Method	Contract Approving Authority	Source of Funds	Est'd. Cost in Lac BDT	Time Code for Process		Invitation for Pre-qualification	Invitation for Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total Time to Contract	Time for Completion of Contract
								Planned dates	Actual Dates									
1		2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
W-20	Construction of Consultants office spaces and Physical Services at PMU office	No	LS	NCB/eGP	PD, MFSP	IDA Credit	60.00											
									Planned dates		1-Nov-22	19-Nov-22	19-Dec-22	26-Dec-22	2-Jan-23	30-Jan-23		30-May-23
									Planned dates									
									Planned dates									
									Planned dates									
									Actual Dates									
W-28	Construction of Steel Silo for Rice at Naogaon	No	1	ICB	CCGP	IDA Credit and GOB	32,550.40											
									Planned dates		22-Aug-22	6-Oct-22	3-Nov-22	2-Jan-23	9-Jan-23	6-Feb-23		5-Feb-25
									Planned dates									
									Planned dates									
									Actual Dates									
W-29	Construction of Sub-station at Dhaka RCF Office for FS&MM System	No	LS	NCB/eGP	PD, MFSP	IDA Credit	50.00											
									Planned dates		1-Sep-22	19-Sep-22	19-Oct-22	26-Oct-22	2-Nov-22	30-Nov-22		30-Mar-23
									Planned dates									
									Planned dates									
									Actual Dates									
Total								32,660.40										

\* Package W-28 Naogaon Silo is a proposed silo; subject to approval of 3rd revision of DPP. Estimated cost is 34.38 Million USD. World Bank will fund, if Bids for the Package W-28 are evaluated and send to Bank for review by the end of Nov/2022.

\*\* Package W-29 is urgently required for power supply to data-center of FS&MM System.

27/11/2022  
 EPRG: SYED RAHMAN  
 Senior Procurement Specialist  
 Modern Food Storage Facilities Project  
 Directorate General of Food, Dhaka

(Muhammad Adnan Rahman)  
 Deputy Project Director  
 Modern Food Storage Facilities Project  
 Directorate General of Food, Dhaka.

১০/১১/২২  
 (মোঃ রেজাউল করিম সোহা)  
 প্রকল্প পরিচালক (উপ-সচিব)  
 আর্থনিক বাণ্য সংরক্ষণার নিয়ন্ত্রণ প্রকল্প  
 খাদ্য অধিদপ্তর, ঢাকা।

১০/১১/২২  
 মোঃ শাখাওয়াত হোসেন  
 মহাপরিচালক  
 খাদ্য অধিদপ্তর, ঢাকা।

১০/১১/২২

# Annual Procurement Plan

Year: 2022-2023

Budget: Development Service

Ministry/Division : Ministry of Food  
 Agency : Directorate General of Food  
 Procuring Entity : Project Director  
 Project/Programme Name & Code : Modern Food Storage Facilities Project 5015

Pack age No.	Description of Procurement Packages Services	Unit	Qty	Procurement Method & Type	Contract Approval Authority	Source of Funds	Estd. Cost in Lac BDT	Time Code for Process	Advertise Eoi	Issue RFP	Technical Proposal Opening	Technical Proposal Evaluation	Financial Proposal Opening & Evaluation	Negotiation	Approval	Signing of Contract	Total Time to Contract Signature	Time for Completion of Contract
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
SD-48	Technical Site Specialist- Civil/Mechanical/ Electrical	No	8	ICSI/ Intermitte nt	PD	IDA Credit	440.00	Planned dates Planned days Actual Dates	1-Nov-22 22 20-Sep-21					23-Dec-22 30	2-Jan-23 10	1-Feb-23 30	92	31-Jan-25 730
Total:							440.00											

*Debsy*  
24/7/2022

*a.f*  
24/7/22

*29/9/22*

*20/11/22*

Engr. Syed Rafiqul Alam  
 Senior Procurement Specialist  
 Modern Food Storage Facilities Project  
 Directorate General of Food, Dhaka

Muhammad Adnan Rahman  
 Deputy Project Director  
 Modern Food Storage Facilities Project  
 Directorate General of Food, Dhaka

(যাঃ রেজাল্টিনা কবিরিয়া সেনা)  
 প্রকল্প পরিচালক (উপ-সচিব)  
 আর্থিক শাখা, সরকারপ্রশাসন বিভাগ, ঢাকা।

মো: শাখাওয়াত হোসেন  
 সহকারী পরিচালক  
 আর্থিক শাখা, সরকারপ্রশাসন বিভাগ, ঢাকা।

65/2



# Modern Food Storage Facilities Project (MFSP)




## Progress of June, 2022& Work Plan FY 2022-23

*(Signature)*

(স্বাঃ সেক্সিওনাল কমিশনার)  
প্রকল্প পরিচালক (উপ-স্টাফ)  
আর্থনিক খাদ্য সরবরাহগোষ্ঠীর নির্মাণ প্রকল্প  
খাদ্য অধিদপ্তর, ঢাকা।

102/10

# Steel Silos: Progress & Work Plan (2022-23)

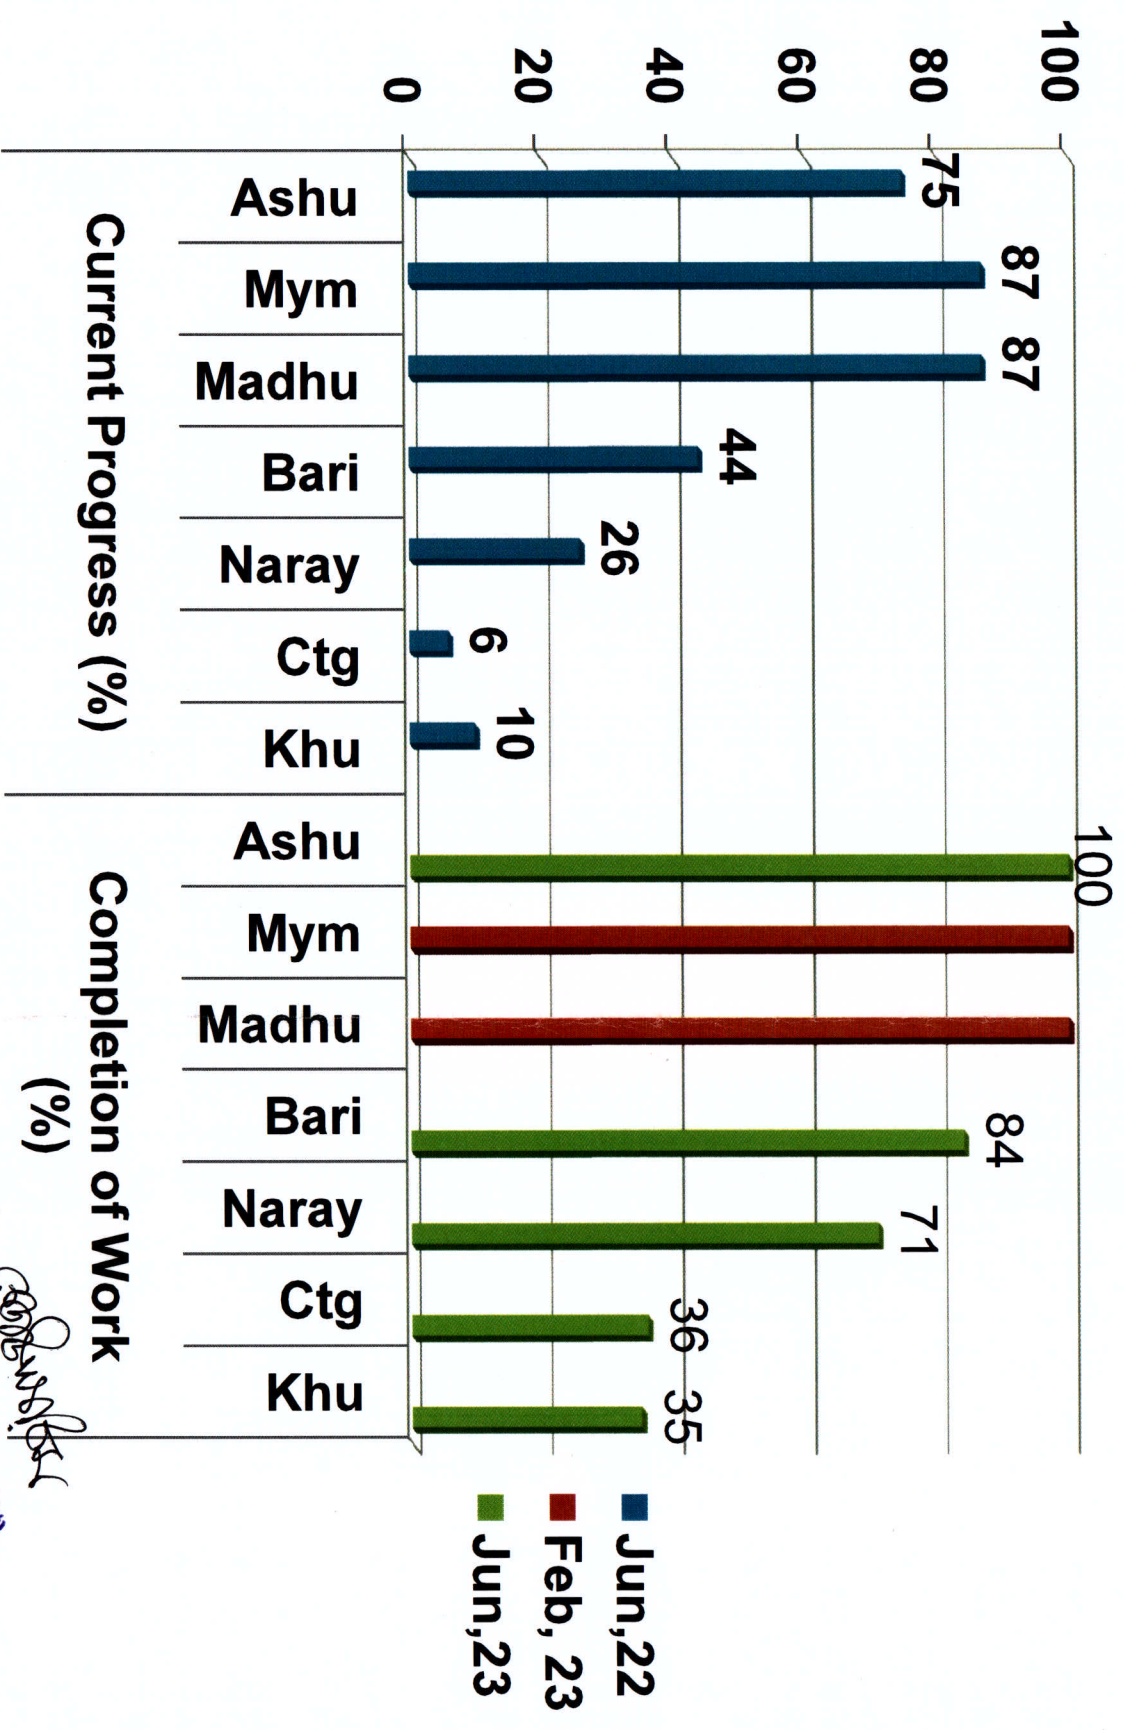


*(Signature)*

(স্বাঃ সেকেন্ডারি কন্ট্রোল সার্ভিস)  
প্রকল্প পরিচালক (উপ-সচিব)  
আঞ্চলিক খাদ্য সংরক্ষণাগার নির্মাণ প্রকল্প  
খাদ্য অধিদপ্তর, ঢাকা।

102/2

# Food Stock & Market Monitoring (ICT): Progress & Work Plan (2022-23)

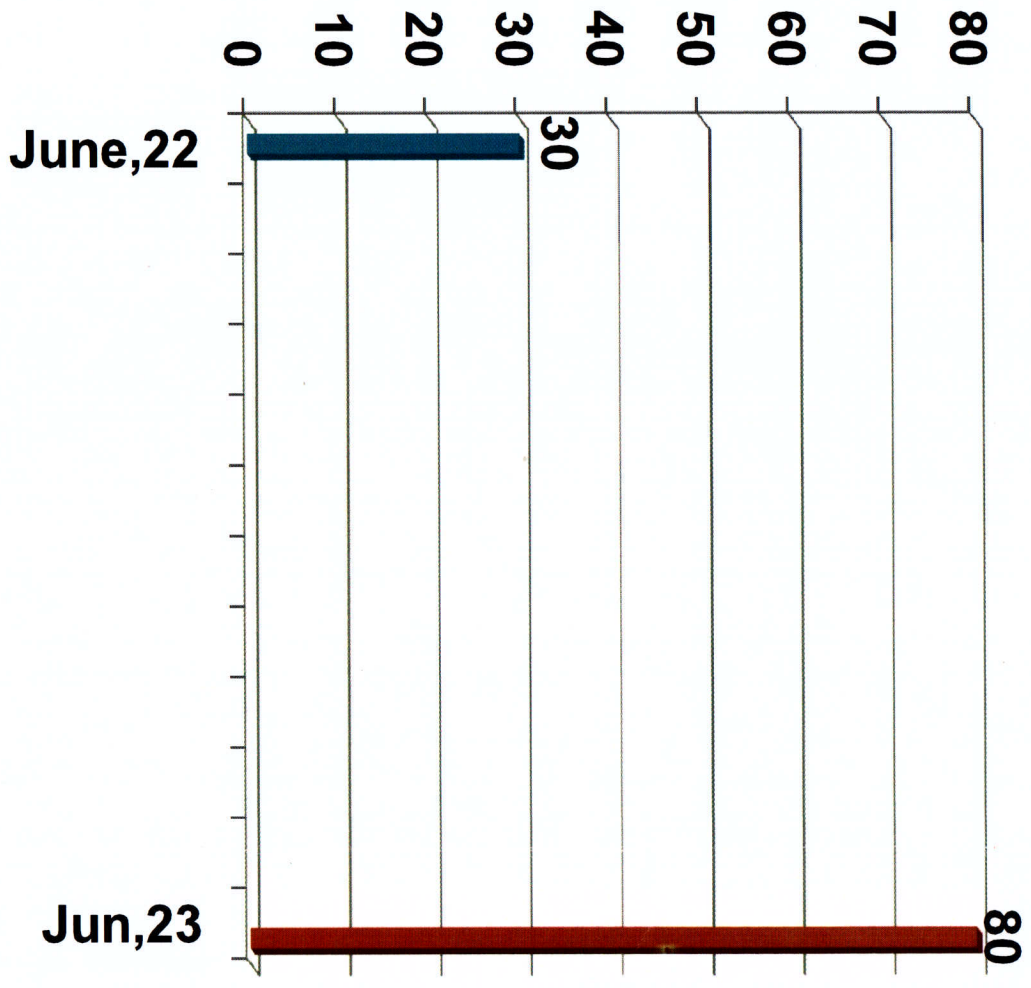


- Current Progress (%)
- Completion of Work (%)

*Foodbank's*  
(सोडो बेजोडना करिमा मेथी)  
बकसो अतिरिक्त (उप-शक्ति)  
बकसो अतिरिक्त (उप-शक्ति) निधिन बकसो  
बकसो अतिरिक्त (उप-शक्ति) निधिन बकसो

১৩/১০

# Integrated Food Policy Research Program (IFPRI): Progress & Work Plan (2022-23)

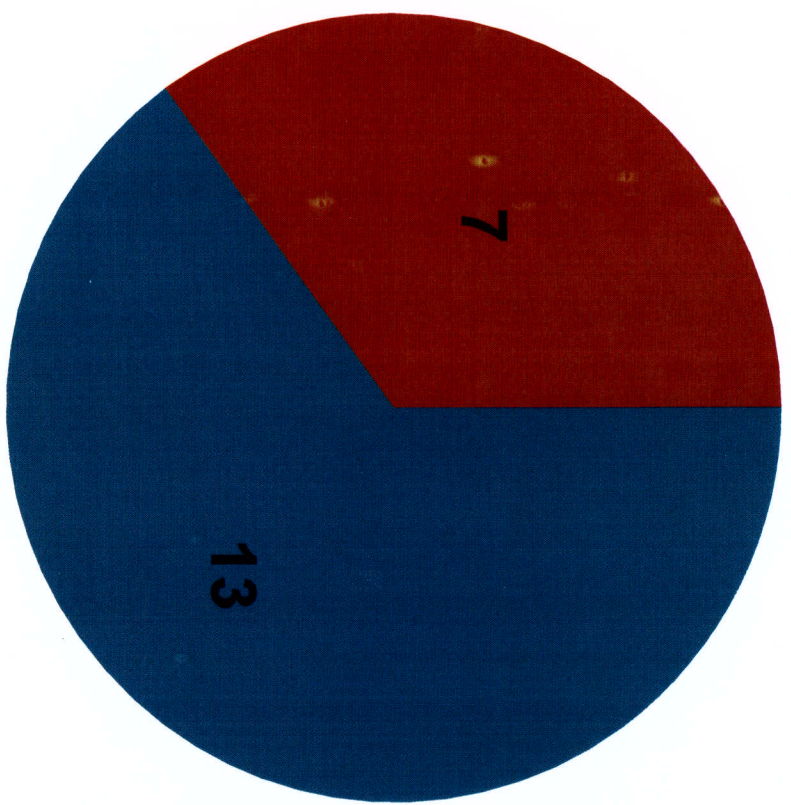

■ Completed (Nos.)

■ Ongoing (Nos.)

7 nos. ongoing study will be completed by June, 2023

*গোবিন্দ চন্দ্র*  
(গোবিন্দ চন্দ্র)  
সিনিয়র প্রোগ্রামার নির্দেশক  
আইসিআর, ঢাকা।
